


International Collaboration and Digital Archives: The Guatemalan National Police Historical Archive Project at UT Austin



Overview

- Background on the (AHPN)
- Live demo of the site
- Discussion of the process and lessons learned
- Significance of the project
- Video

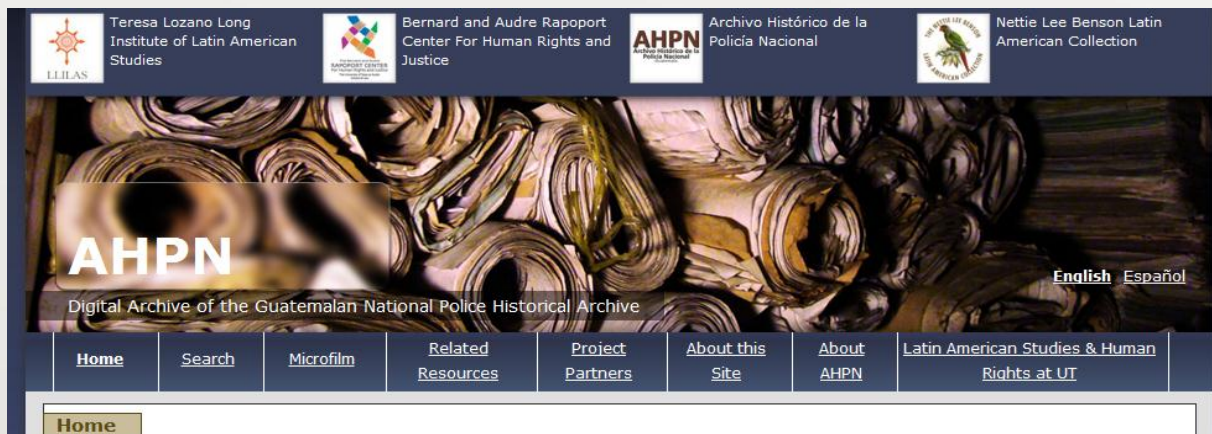

AHPN at a Glance: the physical archive

- Discovered fortuitously in 2005



AHPN at a Glance: the physical archive

- Discovered fortuitously in 2005
- 80 million pages of records



AHPN at a Glance: the physical archive

- Discovered fortuitously in 2005
- 80 million pages of records
- Investigators from Attorney General's office assigned full time at AHPN



AHPN at a Glance: the physical archive

- Discovered fortuitously in 2005
- 80 million pages of records
- Investigators from Attorney General's office assigned full time at AHPN
- Reading room open to the public in 2009



AHPN at a Glance: the digital archive

- 10 million pages of scanned images
- Archival processing, digitization, and metadata creation
- At least 2 million new scanned images per year will be added



Demo

- ahpn.lib.utexas.edu


Collaborative Initiative at various levels

- Within UT Austin
- Within UT Libraries
- Between UT and Guatemala



The Technology

- Apache, Solr, PHP/SQL
- Drupal
- Internet Archive open source page viewer
- TACC's super computers used to generate access derivatives

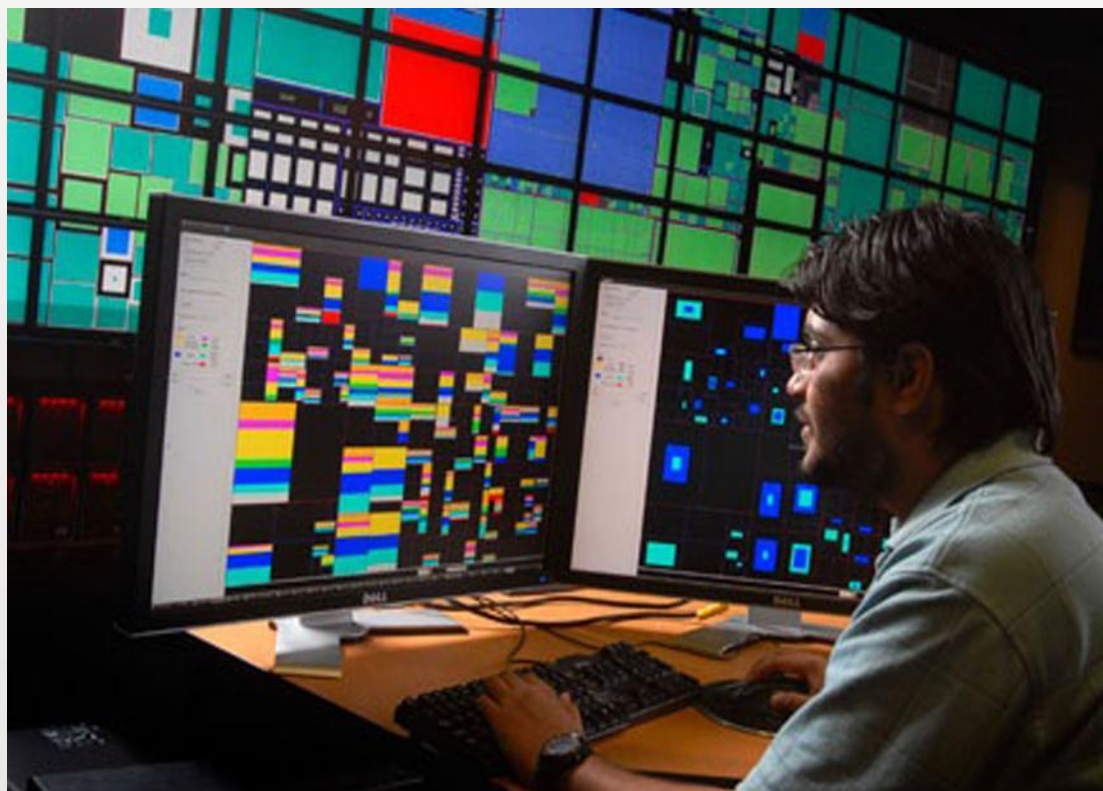

TIS Process

- Stakeholder meetings
- Requirements
- Information Architecture
- Graphic Design
- Front end development and theming
- Testing




Design Challenges

- Sparse and inconsistent metadata
 - OCR not an option
- How to integrate search, how much to emphasize
 - User expectations
- Feedback/approval process
 - Set expectations at outset
 - Meet to review major milestones

Development Challenges

- Massive scale
- Bilingual
- Evaluating and integrating a page viewer

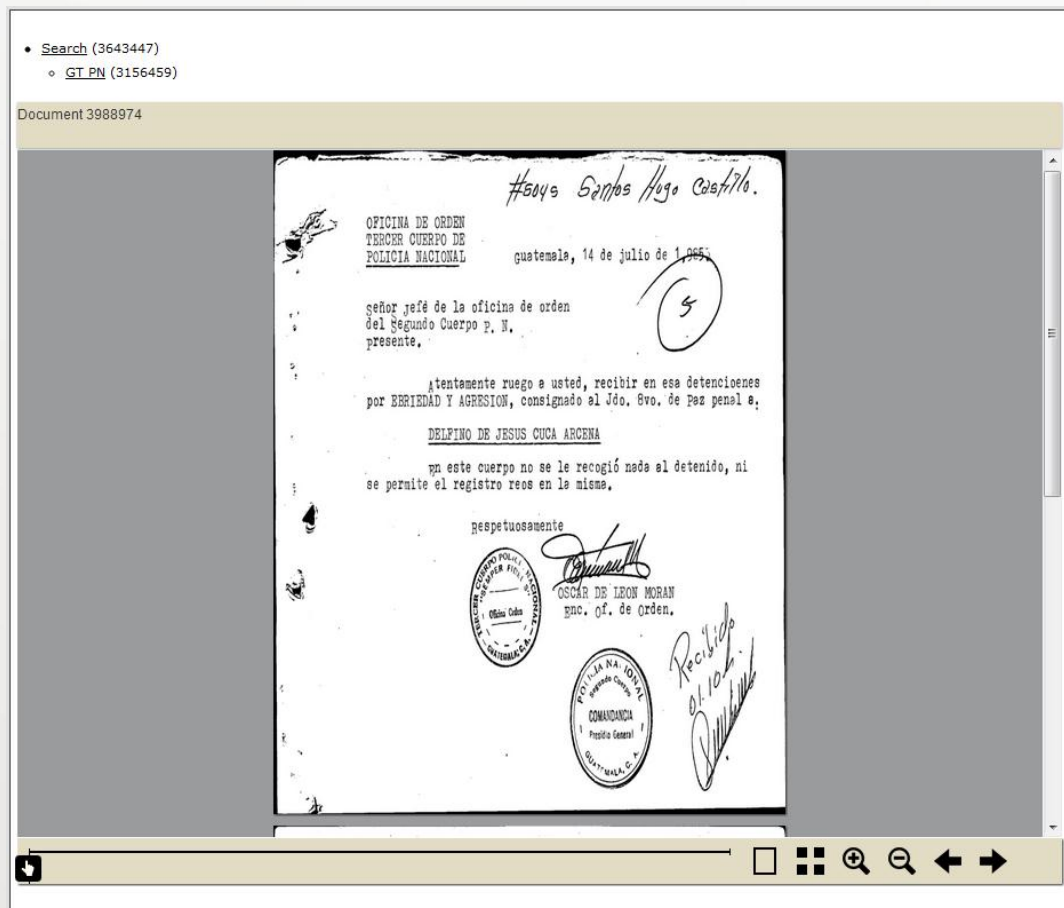

Project Challenges

- Short timeline + hard deadline
- Insufficient time for planning/initiating
- Collaborative nature
- Lost lead programmer halfway through
- Bilingual

Lessons Learned

- Projects of this size and scope will:
 - Have a project plan outlining each person's role
 - Have a project communications plan
 - Involve the right people at the right time
 - Document what's out of scope
 - Have a coordination plan for creating/editing/translating/populating content

Ceremonial Site Launch

- International Conference at UT Dec 2, 2011
- Elections in Guatemala
- Site usage since launch



Project Significance

- Digital libraries as tools for real people
- Uses of AHPN
- Role of Digital Archive

The New York Times

Accused of Atrocities, Guatemala's Ex-Dictator Chooses Silence



Questions or Comments?

Jade Diaz
jade@austin.utexas.edu

Kent Norsworthy
k.norsworthy@austin.utexas.edu



AKPN

**Proceso de Inventario
TRANSFERENCIA**

No. de Acta **52** IDENTIFICACION 000214.
☐ No ☐ Si

Fechas Extremas **1976** **1983**

Conjunto Documental **GT PN 24** Cantidad de Libros **-** Código de Colección **-**

Fecha del Inventario **2010.07.24** Volumen en metros lineales **0.18** Metros.
